


# **Installation Monitoring Report**

Project	NW 2050 Cypress Point	Job Number	24064	RGC N	RGC Number		53216	
Address	7511, 7531, 7651 Minoru Boulevard	Inspector	Matthew	Report	Report Number		26	
	Richmond, B.C.	Weather	Sun / 29°C	Time		1:30pm		
Contractor	Flynn Canada Ltd.	Crew Size	20 Red Sea	al 6	Apprent	ices	12	

Date: July 17, 2025

**Distribution List:** keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

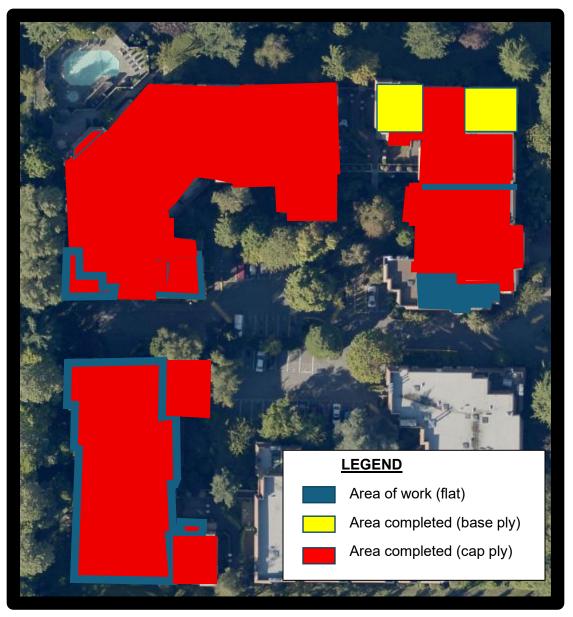

#### 26.1 **Building C**

Gravel stop flashing details on chase flashing application are being stripped in 6" cover strips prior to cap membrane install over top.



#### 26.2 **Building C**

Skylight mock up detail reviewed, interior metal trim flashing to be applied and the blue tarp cut away.



#### 26.3 **Building B**

New load of metal flashing for the parapets has been uploaded, and crew have returned back to continue working on the deck areas.



#### 26.4 **Building B**

Installation of cross broken panels are underway to the parapets.



#### 26.5 **Building B**

S-lock details are being completed at seams which is acceptable.



#### 26.6 Building A

The remaining section of deck has received 2n1 Smart Board sanded with  $\frac{1}{2}$ " HD, securement with 2" Dek fast screws and 2" barbed seam plates.



### 26.7 **Building A**

Elastocol stick adhesive primer application is applied to the installed 2n1 prior to the application of the Sopraply stick traffic cap.



#### 26.8 Building A

Independent cap stripping continued to be rolled into primed surfaces and seams welded closed.



## **Outstanding Items:**

N/A

Reported by:

Matthew Blackstock, RRO Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
