


Installation Monitoring Report

Project	NW 2050 Cypress Point	Job Number	24064	RGC N	RGC Number		53216	
Address	7511, 7531, 7651 Minoru Boulevard	Inspector	Matthew	Report Number		28		
	Richmond, B.C.	Weather	Cloud / 25°C	Time		1:30pm		
Contractor	Flynn Canada Ltd.	Crew Size	18 Red Seal	6	Apprent	ices	8	

Date: July 25, 2025

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

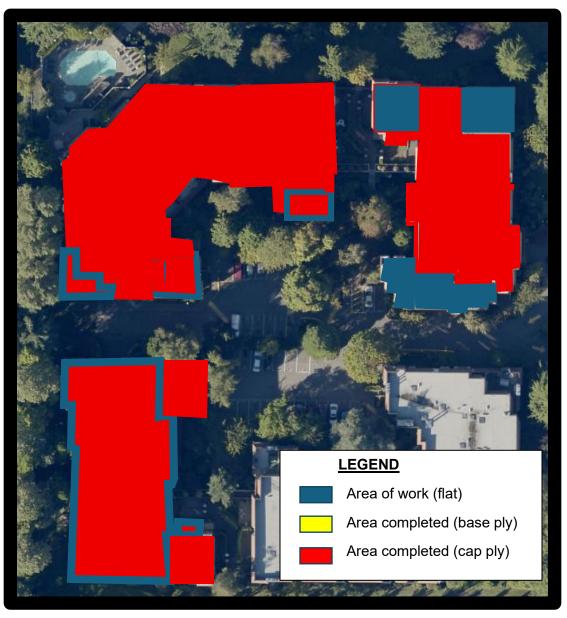

28.1 Building C

The cross broken panel application has finished being applied to the parapets.



28.2 **Building C**

The balance of the cap flashing is being installed along the continuous wind clip. Slocks and standing seam details being applied.



28.3 Building C

Decks are nearly complete being reassembled. Drain screen details as per spec and perimeter fill in remain to be completed.



28.4 **Building B**

Cap flashing and cross broken panel details are nearly completed as well.



28.5 **Building B**

Color matching cladding screw application has begun, Roofing contractor to ensure the specified spacers are installed to ensure the vent strip is open under the cap flashing.



28.6 Building A

The cap membrane application has finished being applied to the deck areas.



28.7 **Building A**

Noted over heated membrane will require repair.



28.8 Building A

Discovered fish mouth in the cap stripping to be repaired.



28.9 Building A

Application of the RS230 lock out details are in progress below door locations.



28.10 Building A

PMMA remains to be extended up the sides.



28.11 Building A

Rubber paver details have begun to be reset back on to the deck areas.



Outstanding Items:

N/A

Reported by:

Matthew Blackstock, RRO Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
