


Installation Monitoring Report

Project	NW 2050 Cypress Point	Job Number	24064	RGC Number		53216	
Address	7511, 7531, 7651 Minoru Boulevard	Inspector	Matthew	Report Number		29	
	Richmond, B.C.	Weather	Sun / 28°C	Time		1:30pm	
Contractor	Flynn Canada Ltd.	Crew Size	16 Red Seal	6	Apprent	ices	8

Date: July 29, 2025

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

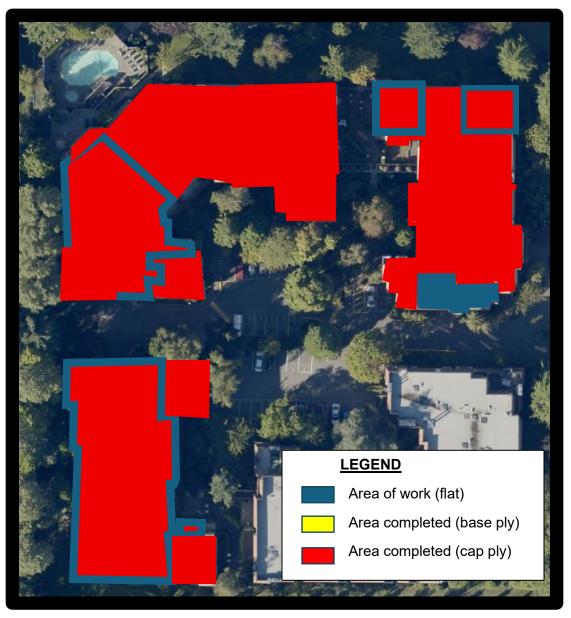

29.1 Building C

The balance of the cap flashing installation is nearly completed to the main roof area.



29.2 Building C

Fire wall flashing detail extends up and ties into the wall panels and cap flashing in an acceptable manner.



29.3 **Building C**

Standing seam details appear acceptable, flashing foreman to ensure a positive drainage slope is achieved.



29.4 Building C

Privacy screens are being reset into place, the balance of pavers around the perimeter and drain screen details to be applied.



29.5 **Building B**

Installation of the 24ga cross broken panels and cap flashing continues to be applied towards the scaffolding.




29.6 **Building B**

Flashing transition to the cap detail is acceptable. Cladding screws with spacers remains to be applied at the perimeter.



29.7 **Building B**

Application of the double gum lip to the base of the elevator shaft roof in progress.

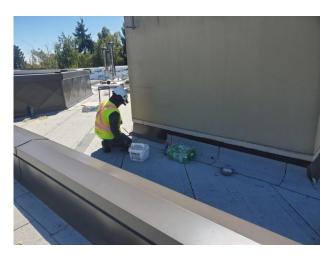

29.8 Building A

Rubber & concrete paver installation is nearly completed to the deck areas.



29.9 Building A

Requested paver repositioning to move the privacy screen away from the vents for easier cleaning of the ducts.



Outstanding Items:

• 28.8

Reported by:

Matthew Blackstock, RRO Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
