


Installation Monitoring Report

Project	NW 2050 Cypress Point	Job Number	24064 RGC Number		53216		
Address	7511, 7531, 7651 Minoru Boulevard	Inspector	Matthew	Report Number		32	
	Richmond, B.C.	Weather	Sun / 25°C	Time		12:30am	
Contractor	Flynn Canada Ltd.	Crew Size	12 Red Seal	4	Apprent	ices	6

Date: August 7, 2025

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

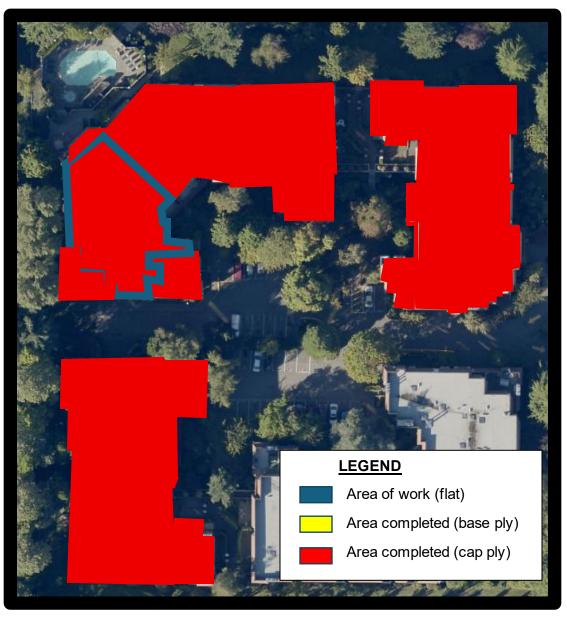

32.1 **Building A**

Decks and roof areas are now ready for installation of wall metal panels and cap flashing.



32.2 **Building B**

Clean up on the building is underway, unnecessary equipment and materials downloaded.





32.3 **Building B**

Color matching gasketed cladding screws and standoff installation on the inside face of the cap flashing is underway.




32.4 **Building B**

Counter flashing around the base of the skylights are being installed and secured with hidden clips and fasteners.



32.5 **Building B**

The second gum lip flashing is being installed around the base of the elevator shaft roof.

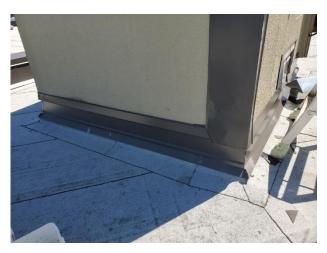

32.6 **Building B**

Sealant application remains to be applied.




32.7 **Building B**

Final details to the deck areas are underway.



32.8 **Building B**

Missing debris screen to be installed at drain on noted deck.

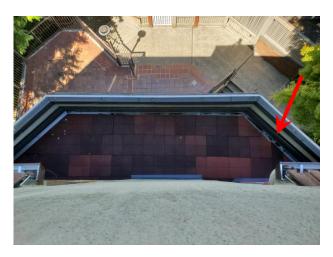

32.9 **Building B**

New skylight installation is completed on the noted deck area and privacy screen set in place.



32.10 **Building B & C**

Scaffolding in progress of being removed from between the noted buildings.



Outstanding Items:

• Item #31.2 - Strata council to review.

Reported by:

Matthew Blackstock, RRO Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
