


# **Installation Monitoring Report**

Project	NW 2050 Cypress Point	Job Number	24064	RGC Number		53216	
Address	7511, 7531, 7651 Minoru Boulevard	Inspector	Matthew Report Number		Number	34	
	Richmond, B.C.	Weather	Sun / 29°C	Time		1:30pm	
Contractor	Flynn Canada Ltd.	Crew Size	6 Red Seal	3	Apprent	ices	3

**Date:** August 13, 2025

**Distribution List:** keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

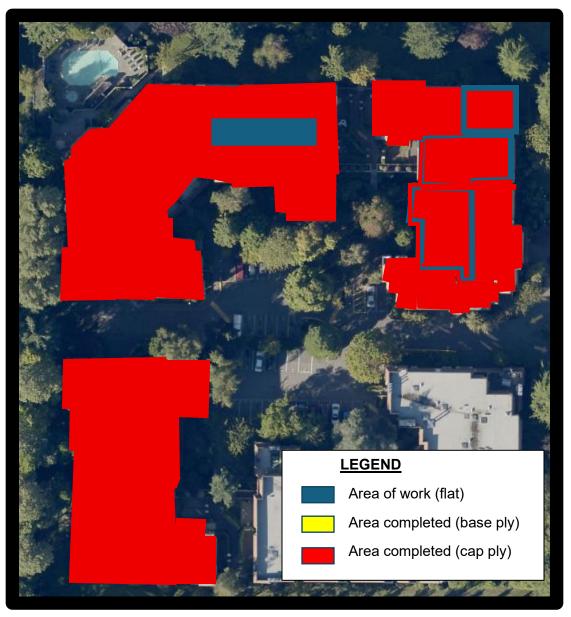

## 34.1 Building A

Installation of flashing to the perimeter of the main roof has begun.



#### 34.2 **Building A**

Perforated vent strip is being applied over the wall vent opening as per specifications.



# 34.3 **Building A**

Base wall flashing is being set in place and secured with pan head screws.



#### 34.4 **Building A**

Saddle flashing chimney chase details are being worked on. A continuous 24ga wind clip is being applied to the exterior face of the parapet.



## 34.5 **Building A**

Installation of base wall flashing has also begun on the Northeast deck.



#### 34.6 **Building C**

Pre-final carried out with Roofing Superintendent present.

Noted partially open seams to be corrected.




## 34.7 **Building C**

Scuff marks and stains to be repaired with Alsan flashing and color matching granules.



## 34.8 **Building C**

Contractor pavers with XPS remain to be placed at roof hatch and tops of the hatches to be painted.



# **Outstanding Items:**

• Item #31.2 = Strata council to review.

Reported by:

Matthew Blackstock, RRO Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
