


Installation Monitoring Report

Project	NW 2050 Cypress Point	Job Number	24064	RGC Number		53216	
Address	7511, 7531, 7651 Minoru Boulevard	Inspector	Matthew Report Number		35		
	Richmond, B.C.	Weather	Cloud / 24°C	Time		12:30pm	
Contractor	Flynn Canada Ltd.	Crew Size	10 Red Seal	4	Apprent	ices	3

Date: August 18, 2025

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

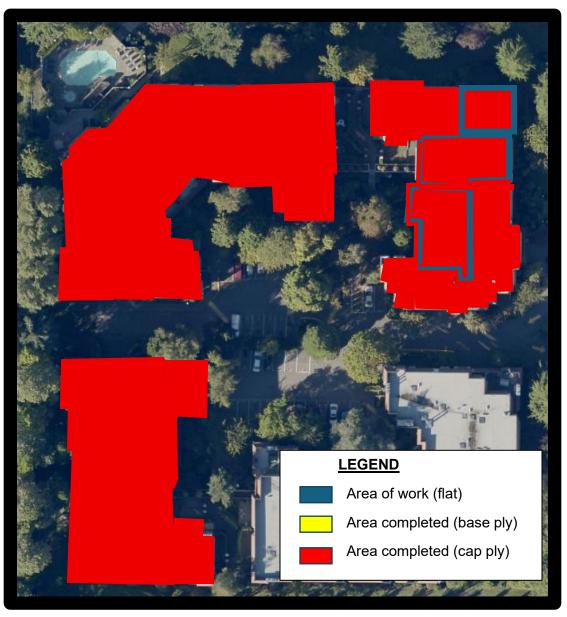

35.1 Building A

Cap flashing installation continues on all work elevations. Standing seam and Slocks are being used at flashing connections.



35.2 **Building A**

Continuous wind clip installation with front face securement is under way prior to cap flashing application.



35.3 Building A

Wall panels are loaded to the roof area. Roofing contractor to ensure the panels are 4' in length as per specifications.



35.4 **Building A**

Saddle detail tie in found acceptable.



35.5 **Building A**

Alsan flashing application to the base of galvanized flashing found acceptable.



Outstanding Items:

• Items #34.6 - 34.8

Reported by:

Matthew Blackstock, RRO Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
