


Installation Monitoring Report

Project	NW 2050 Cypress Point	Job Number	24064	RGC Number		53216	
Address	7511, 7531, 7651 Minoru Boulevard	Inspector	Ted	Report Number		38	
	Richmond, B.C.	Weather	Sun / 22°C	Time		9:25am	
Contractor	Flynn Canada Ltd.	Crew Size	5 Red Seal	3	Apprenti	ces	2

Date: August 26, 2025

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

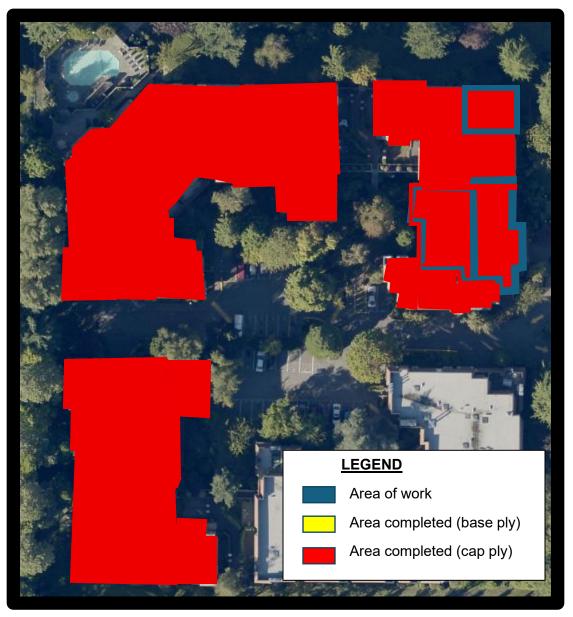

38.1 Building A

Stair tower and roof access area is tidy at the outside.



38.2 **Building A**

Southwest deck - the caulking applied to the storm collar is messy. Remove and recaulk with grey sealant as has been used elsewhere.



38.3 **Building A**

Temporary seal noted at rain cap with pipe penetration.



38.4 Building A

Crew are working at various areas.



38.5 **Building A**

Fire wall detail is 95% complete.



38.6 **Building A**

It was noted that the 22ga galvanized secondary flashing is offset from the primary 24ga painted flashing as required.



38.7 **Building A**

Fastener spacing in the wind clip is 12" - 16" o/c.



38.8 Building A

Clips are installed at the standing seam corners.



38.9 Building A

Sheet metal worker observed completing a standing seam corner detail.



38.10 Building A

Wall flashing and bug screen are now complete.



38.11 Building A

Wall panel secured with 3 sheet metal screws.



38.12 Building A

Wall panels observed being installed.



38.13 Building A

Saddle details are complete in areas.



38.14 **Building A**

Gap in fabrication needs to be closed off at the Southeast upper chimney. Gap due to variation in roof deck height.



38.15 **Building A**

Repair patch of SBS is defective. This will require a further repair patch or coating.



Outstanding Items:

• Items #34.6 – 34.8

Reported by:

Ted Neef RRO
Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
