


# **Installation Monitoring Report**

Project	NW 2050 Cypress Point	Job Number	24064	RGC Number		53216	
Address	7511, 7531, 7651 Minoru Boulevard	Inspector	Matthew	Report Number		40	
	Richmond, B.C.	Weather	Sun / 24°C	Time		12:00pm	
Contractor	Flynn Canada Ltd.	Crew Size	7 Red Seal	3	Apprenti	ices	2

Date: September 2, 2025

**Distribution List:** keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

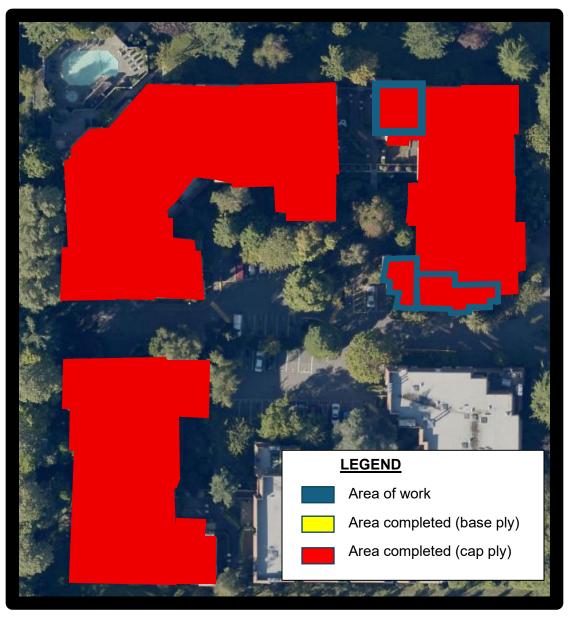

#### 40.1 Building A

Flashing installation continues on the South and Northwest deck areas.



#### 40.2 **Building A**

Counter flashing has been fitted and secured along the base of walls. Secured with color matching gasketed cladding screws.



#### 40.3 **Building A**

Standing seams are being applied to corners in an acceptable manner.



#### 40.4 **Building A**

Damaged gravel stop flashing and lifting membrane to be repaired.



### 40.5 **Building A**

Alsan flashing to be applied with taped edges and granules over top along membrane termination.



#### 40.6 **Building A**

Corner trim to be reset back into place with carpentry finishing nails and repainted.



#### 40.7 Building A

The wood trim to be reset back into place below windows, must be painted to match pre-existing.



#### 40.8 Building A


Door back dam and threshold flashing to be installed back into place.



## 40.9 **Building A**


Installation of new pavers at the perimeter must not be smaller than half a paver size.

Small pieces of paver will not be accepted, a course of a half paver in the field will be accepted to ensure that a full paver can be used at the perimeter.

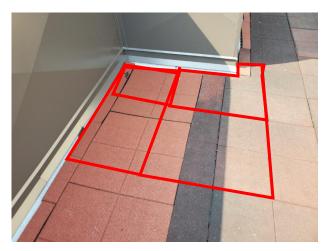

## 40.10 **Building B, Unit 324**


In two locations, missing s-lock details to have the flashing removed and replaced with new.

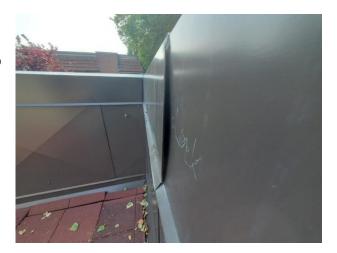



# 40.11 **Building B, Unit 324**

Standing seam details are to match at corners.



#### 40.12 **Building B, Unit 324**

Poorly fitted BUR hood to be corrected.



## 40.13 **Building B, Unit 324**

Similar paver fitting to be applied to the deck area. No smaller than half paver to be used and damaged pavers to be removed.



## **Outstanding Items:**

• Items #34.6 - 34.8, #39.7

Reported by:

Matthew Blackstock, RRO Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
