


Installation Monitoring Report

Project	NW 2050 Cypress Point	Job Number	24064	RGC Number		53216	
Address	7511, 7531, 7651 Minoru Boulevard	Inspector	Matthew	Report Number		48	
	Richmond, B.C.	Weather	Light Rain / 20°C	Time		11:45am	
Contractor	Flynn Canada Ltd.	Crew Size	4 Red Seal	0	Apprent	ices	0

Date: October 1, 2025

Distribution List: keith.lodge@flynncompanies.com, ken.brown@flynncompanies.com, nw2050@telus.net. matt@phoenixroofconsultants.ca

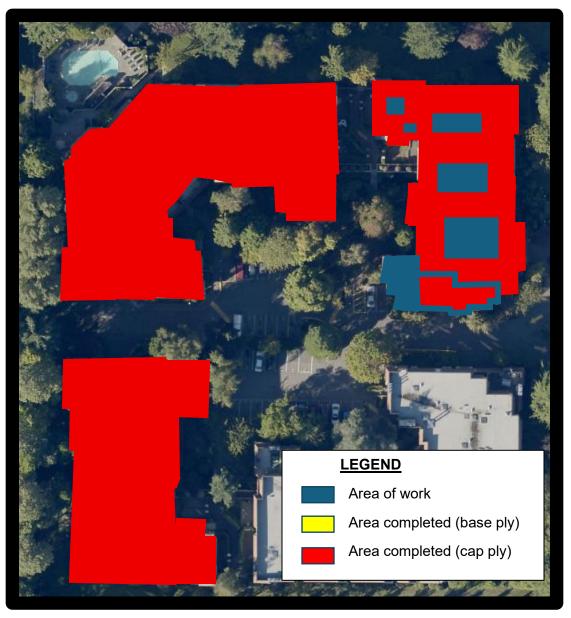


48.1 Building A

Pavers around the drain body have been leveled out as required.




48.2 **Building A**

Rubber pavers around the perimeter are being corrected.



48.3 **Building A**

Counter flashing installation and prep for skylight install underway.

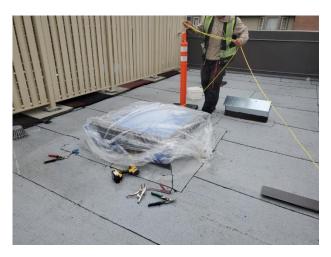

48.4 Building A

Two skylights were sent as standards and not opening. Foreman indicated that opening skylights have been ordered.



48.5 **Building A**

Fasteners for the exterior frame to be installed.



48.6 **Building A**

Details on the lower Northwest deck are near completed.



48.7 **Building A**

The balance of pavers, privacy screen installation and debris removal to be completed on the noted deck area.



48.8 Building A

Scaffolding material to be removed from the roof surface.



Outstanding Items:

• Items #34.6 – 34.7, #39.7, #40.5, 45.6, #46.1 & 46.3

Reported by:

Matthew Blackstock, RRO Phoenix Roof Consultants

Phoenix Roof Consultants field reviews are for general conformance to specifications and roofing compliance only. Our reviews are not to take the place of the contractor's own quality control which shall remain the responsibility of the contractor. Phoenix Roof Consultants will not be responsible for acts or omissions of the contractor or for the contractor's failure to fulfill the intent of the specifications, contract, or quote.
